



October 19, 2023

Ref: 42149.04

George K. McGregor, AICP
Planning & Community Development Director
Town of Simsbury
933 Hopmeadow Street
Simsbury, CT 06070

Re: Master Site Development Plan Submission – 200 Hopmeadow Street – Supplemental Information

Mr. McGregor,

The following items are enclosed as requested to support the Master Site Development Plan submission for the proposed Ridge at Talcott Mountain South located at 200 Hopmeadow Street in Simsbury.

- 1. Three (3) 30"X42" full size copies of the Master Site Development Landscape Plan dated September 25, 2023.
- 2. Five (5) 11"x17" copies of the revised Site Schedule.
- 3. Five (5) 11"x17" copies of the phasing plan in conceptual mapped format.
- 4. One (1) 8.5"x11" copy of the bedroom breakdown titled "Building Types".
- 5. Five (5) copies of the WPCA Updated Sanitary Sewer allocation letter addressed to SL Simsbury LLC dated October 16, 2023.

In addition, a viewshed analysis of the site from Hopmeadow Street is currently being worked on and will be submitted under separate cover.


Please contact me at 860-807-4379 or <u>pvitaliano@vhb.com</u> if you have any questions, comments or require additional information. Thank you.

Sincerely,

Paul Vitaliano, P.E.

CT Director of Land Development pvitaliano@vhb.com





WATER POLLUTION CONTROL 36 Drake Hill Road Simsbury, Connecticut 06070

October 16, 2023

SL Simsbury LLC 788 Morris Turnpike Short Hills, NJ 07078

Re: Updated Sanitary Sewer allocation for South Site, 200 Hopmeadow, Simsbury, CT

Dear sir:

The sewer allocation for the South Site, 200 Hopmeadow, Map Block lot F17-154-009-2, Simsbury, CT was approved by the Simsbury Water Pollution Control Authority (WPCA) at its June 8, 2023 meeting. This allocation was based on the 124.64-acre site with an underlying zoning of I1. This acreage is based on the Town of Simsbury assessor's cards and submitted development plans. A wetland survey completed in 1997 was used to determine usable acreage.

The new proposed development of 580 units, comprising of 216-1 bedroom, 296-2 bedroom, 32-3 bedroom, and 36-4 bedroom units would require an estimated flow of 121,576 gallons/day of the 334,880 gallons/day available from the site.

A facility Connection Charge (FCC) for each building will be determined upon submittal of plans. The FCC compensates for infrastructure investment that has and is being made to provide sewer service. Simsbury's wastewater collection and treatment systems are solely supported by customer fees. The FCC is due when the sewer connection permit is obtained.

Please call, 860-658-3258, if you have any questions.

Sincerely,

Anthony Piazza Superintendent


Enclosure

Cc: P. Gilmore, Chairman WPCA


- T. Roy, Director Public Works
- G. McGregor, Director of Community Planning & Development
- H. Miga, Building Official

Telephone (860) 658-3258 Facsimile (860) 658-6809 www.simsbury-ct.gov

An Equal Opportunity Employ 7:00 – 3:30 Monday through Frid



	Building Types							
Building Type	Qty.	Units/ Bldg.	Total units	BR	2 BR	3 BR	4 BR	Total BRs
Garages	11	Ø	Ø	Ø	Ø	Ø	Ø	Ø
Community Bldg	1	Ø	0	Ø	Ø	0	0	Ø
3-Story Apt.	4	32	128	56	72	Ø	Ø	200
4-Story Apt.	8	45	360	160	200	Ø	Ø	560
Duplex-1	5	2	10	Ø	10	0	0	20
Duplex-2	٦	2	14	Ø	14	Ø	Ø	28
SF-IA	11	1	11	Ø	Ø	11.	Ø	33
SF-IB	13	1	13	Ø	Ø	Ø	13	52
SF-2A	11	1	11	Ø	Ø	11	Ø	33
SF-2B	12	1	12	Ø	Ø	Ø	12	48
SF-3A	10	1	10	Ø	Ø	10	Ø	3Ø
SF-3B	11	1	11	Ø	Ø	Ø	11	, 44
Total	104		580	216	592	96	144	1,048

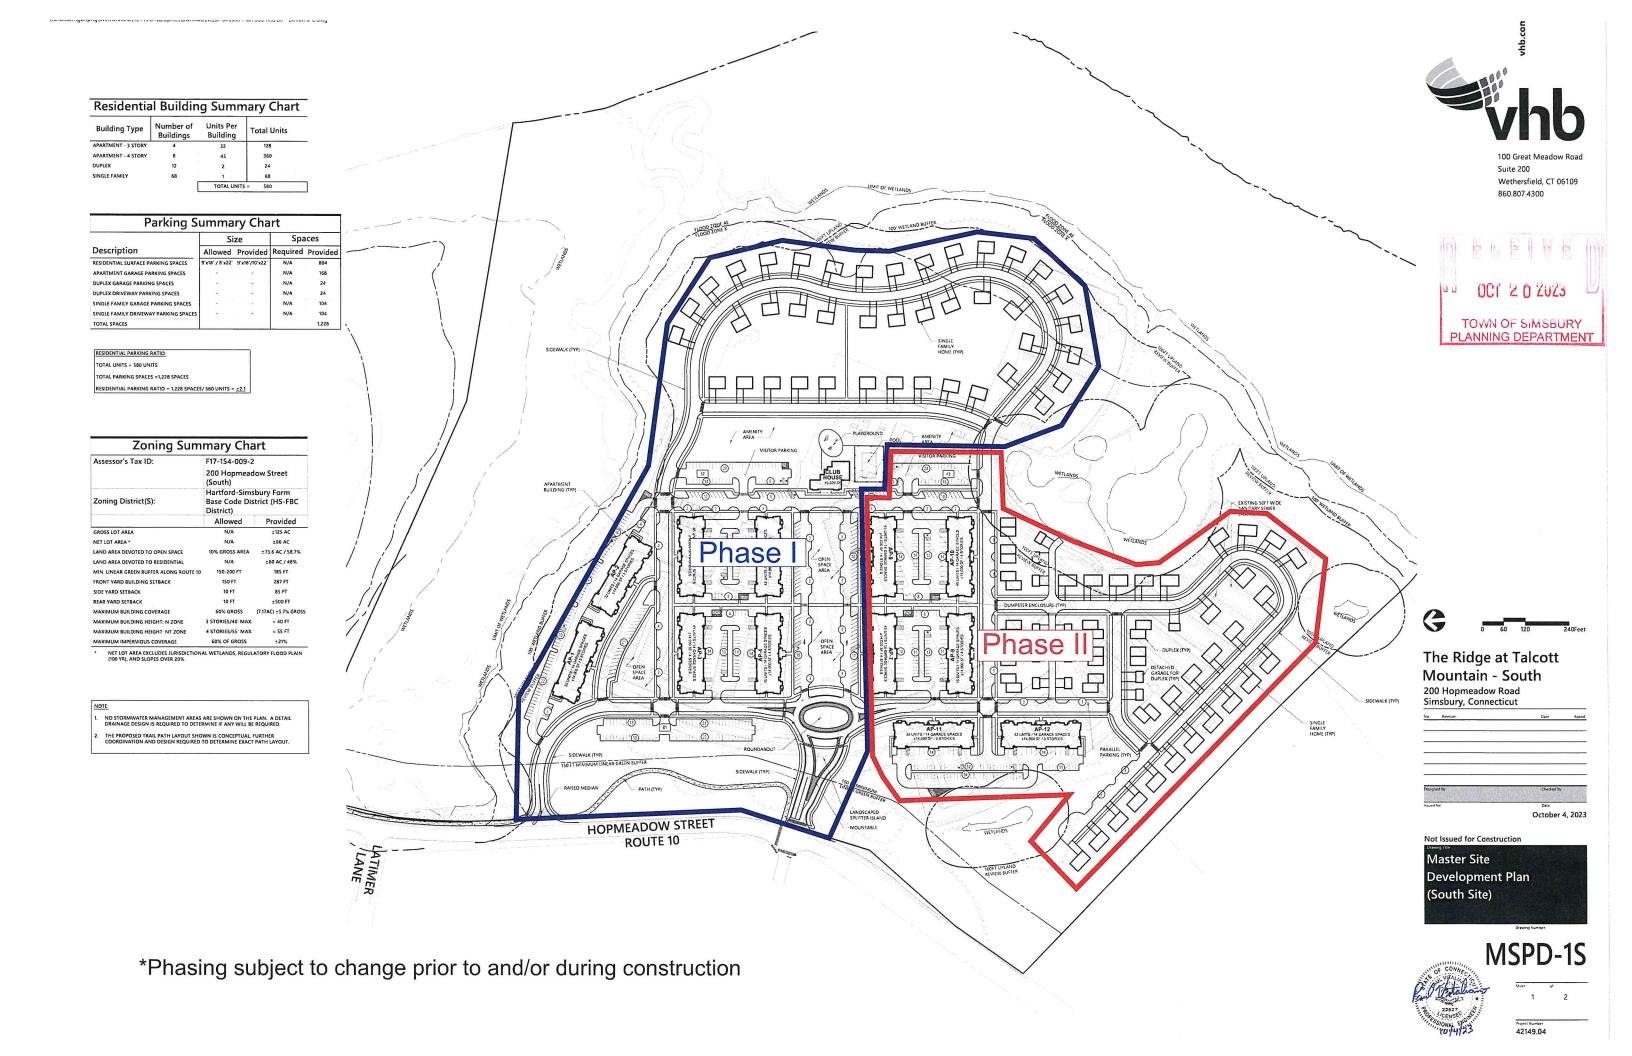





)	Task Name	Duration	Start	Finish	Qtr 4, 2022 Qtr 1, 2023 Qtr 2, 2023 Qtr 3, 2023 Qtr 4, 2023 Qtr 1, 2024 Qtr 2, 2024 Qtr 3, 2024 Qtr 4, 2025 Qtr 2, 2025 Qtr 3, 2025 Qtr 3, 2025 Qtr 2, 2025 Qtr 3, 2026 Qtr 3, 2026 Qtr 3, 2026
	Pre- Application Meetings	66 days	Thu 6/1/23	Thu 8/31/23	Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Ap
					Pre- Application Meetings 8/31
2	Master Plan Site Development Application	66 days	Mon 10/2/23	Sun 12/31/23	Master Plan Site Development Application 12/31
3	Site Plan Development	87 days	Mon 1/1/24	Tue 4/30/24	Site Plan Development 4/30
4	IWWA Permitting	23 days	Wed 5/1/24	Fri 5/31/24	IWWA Permitting 5/31
5	Design Review Board Permitting	23 days	Wed 5/1/24	Fri 5/31/24	Design Review Board Permitting 5/31
6	Zoning Comission Permitting	44 days	Wed 5/1/24	Sun 6/30/24	
7	DOT OSTA Permitting	176 days	Mon 1/1/24	Sat 8/31/24	Zoning Comission Permitting 6/30
8	Construction Plan Development	89 days	Mon 7/1/24	Thu 10/31/24	DOT OSTA Permitting 8/31
	Encroachment Permit Process	89 days	Tue 10/1/24		Construction Plan Development 10/31
					Encroachment Permit Process 1/31
10	Construction	433 days?	Fri 11/1/24	Tue 6/30/26	Construction 6/30
11	Site Work	433 days	Fri 11/1/24	Tue 6/30/26	Site Work 6/30
12	Erosion control	20 days	Fri 11/1/24	Thu 11/28/24	Erosion control 11/28
13	Clearing	25 days	Fri 11/1/24	Thu 12/5/24	Clearing 12/5
14	Grading, Cut/Fill	369 days	Fri 11/1/24	Wed 4/1/26	Grading, Cut/Fill
15	Drainage/Roadwork	413 days	Sun 12/1/24	Tue 6/30/26	
16	Building Construction	367 days?	Mon 2/3/25	Tue 6/30/26	
17	Phase I	367 days	Mon 2/3/25	Tue 6/30/26	Building Construction 6/30
18	Apartment Building's 1-6				Phase I parameter 1 6/30
		183 days		Wed 10/15/25	Apartment Building's 1-6 10/15
19	Single Family Homes 1-41	183 days		Wed 10/15/25	Single Family Homes 1-41 10/15
20	Club House	307 days	Mon 2/3/25	Tue 4/7/26	Club House 4/7
21	Phase II	208 days	Sun 9/14/25	Tue 6/30/26	Phase II
22	Apartment Buildings 7-12	183 days	Sun 9/14/25	Tue 5/26/26	Apartment Buildings 7-12
23	Duplex's 1-12	208 days	Sun 9/14/25	Tue 6/30/26	Duplex's 1-12
24	Singe Family Homes 42-68	123 days	Sun 9/14/25	Tue 3/3/26	
					Singe Family Homes 42-68 3/3

